

# klia 2

## MAINTENANCE PROGRESS

In this latest report series, we are pleased to share that we had completed a total of five locations at the parking apron. This has accumulated to a total of 54 locations altogether.

In Phase 2, we will extend the grouting injection method to 40 locations, inclusive of several newly identified areas and a few areas that had been maintained in 2015. Phase 2 is determined to further improve the occurrence of pavement depressions.

Grouting injection works for Phase 2 started in September 2016 and currently at 32.5% completion.

Grouting injection remains the method of choice as it provides less disruption to the terminal operations.



### GROUTING INJECTION WORKS MASTERPLAN (AS AT 30 SEPTEMBER 2016)

Malaysia Airports has started its second phase of grouting injection works in August 2016 and as at 30 September, we had completed a total of 5 locations on the parking apron.


#### GROUTING INJECTION MASTERPLAN

- Completed Area for Phase 1 (Precast Slab & Grouting Injection) ■
- Planned Area for Phase 2 (Grouting Injection) ■
- Completed Area for Phase 2 (Grouting Injection) ■
- Work-in-Progress for Phase 2 (Grouting Injection) ■

**Completed:**  
13/40 locations (33%)

Parking Apron: 9/26 bays (35%)

Taxiway: 4/14 taxiways (29%)

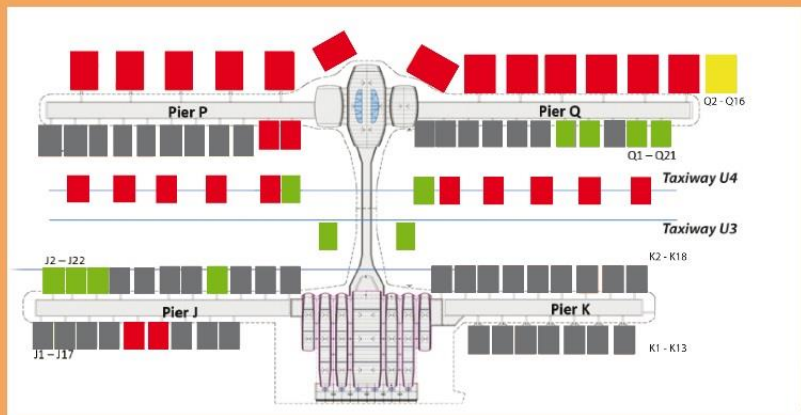

### kli2 Recorded 5.9% Growth for Passenger Movements from Jan-Sep 2016



	2016	2015	(%)
<b>International</b>	27,191,768	25,814,264	5.3%
<b>Domestic</b>	11,257,783	10,486,658	7.4%
<b>TOTAL</b>	<b>38,449,551</b>	<b>36,300,952</b>	<b>5.9%</b>

For the last nine month, the total number of passengers at kli2 for both international and domestic flights registered 5.9% growth with 38 million passengers in 2016 compared to 36 million passengers for the same period in 2015.

Malaysia Airports takes our responsibility towards public safety very seriously. Thank you for your patience and understanding.
