

klia 2

MAINTENANCE PROGRESS

In this latest report series, we are pleased to share that we had completed a total of four locations at the parking apron and another three locations on the taxiways. This has accumulated to a total of 49 locations altogether and marked the completion of Phase 1 of the maintenance work progress in klia2.

In Phase 2, we will extend the grouting injection method to 40 locations, inclusive of several newly identified areas and a few areas that had been maintained in 2015. Phase 2 is determined to further improve the occurrence of pavement depressions.

Grouting injection works for Phase 2 started in August 2016 and currently at 20% completion.

Grouting injection remains the method of choice as it provides less disruption to the terminal operations.



GROUTING INJECTION WORKS MASTERPLAN (AS AT 31 AUGUST 2016)

Malaysia Airports has started its second phase of grouting injection works in August 2016 and as at 31 August, we had completed a total of 8 locations comprising 4 locations on the parking apron and another 4 locations on the taxiway.

GROUTING INJECTION MASTERPLAN

Completed Area for Phase 1
(Precast Slab & Grouting Injection)

Planned Area for Phase 2
(Grouting Injection)


Completed Area for Phase 2
(Grouting Injection)

Work-in-Progress for Phase 2
(Grouting Injection)

Completed:
8/40 locations (20%)

Parking Apron: 4/26 bays (15%)

Taxiway: 4/14 taxiways (29%)

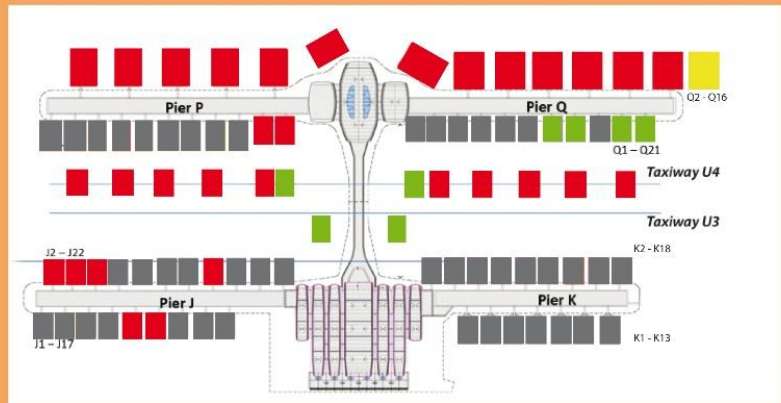

klia2 Recorded 6.1% Growth for Passenger Movements from Jan-Aug 2016



	2016	2015	(%)
International	12,085,724	10,966,262	10.2%
Domestic	5,864,010	5,952,962	-1.5%
TOTAL	17,949,734	16,919,224	6.1%

On a last-eight-month basis, the total number of passengers at klia2 for both international and domestic flights registered 6.1% growth with 18 million passengers in 2016 compared to 17 million passengers for the same period, January to August in 2015.

Malaysia Airports takes our responsibility towards public safety very seriously. Thank you for your patience and understanding.
